






ID	Task Mode	Task Name	Duration	% Complete	Start
1	✓	Milestone 1 Nestucca K-8 Expansion (Authorization to Proceed)	0 days	100%	Fri 1/3/20
2	✓	Milestone 2 Mobilization Start of phase 2	0 days	100%	Mon 1/13/20
3		Nestucca K-8 Expansion (whole project duration)	457.5 days	18%	Mon 12/2/19
4		Project Submittals	125 days	69%	Mon 12/2/19
5	✓	Concrete	10 days	100%	Mon 12/2/19
6	✓	Steel Rebar	15 days	100%	Mon 12/2/19
7	✓	Plumbing Underground	15 days	100%	Mon 12/2/19
8	✓	Electrical Underground	2 days	100%	Mon 12/2/19
9		Steel Columns, HSS headers, buckets, ships ladders,	20 days	85%	Mon 1/6/20
10	✓	High Wall Engineered Bracing Plan	10 days	100%	Mon 2/3/20
11		Framing package and hardware	20 days	50%	Mon 2/3/20
12		Trusses	20 days	50%	Mon 2/3/20
13		Storefront, Windows, Doors and Hardware	20 days	50%	Mon 2/3/20
14		MEP	20 days	50%	Mon 3/2/20
15		Long lead Items	20 days	50%	Mon 3/2/20
16		Commercial Kitchen equipment	20 days	50%	Mon 3/30/20
17	✓	Playground equipment	20 days	100%	Mon 3/30/20
18		Finishes	20 days	50%	Mon 4/27/20
19		Phase 1 Demolition, Excavation, Trenching and Utilities	92 days	76%	Mon 12/2/19
20	✓	Preconstruction Meeting Earthwork, Concrete, Utilities and Trenching	92 days	100%	Mon 12/2/19
21	✓	Call for Dig alert number	1 day	100%	Mon 12/2/19
22	✓	Baricade walls as needed to begin Vertical Construction	15 days	100%	Mon 12/2/19
23	✓	Complete Section under at Drive Isle	10 days	100%	Mon 3/9/20
24	✓	Area A Gridlines A-B 4-18	46.5 days	100%	Mon 12/2/19
25	✓	Remove lead contaminated materials	7 days	100%	Mon 12/2/19
26	✓	Demolition in preparation for phase 1 foundations	7 days	100%	Mon 12/9/19
27	✓	Stake building Corners and columns	2 days	100%	Mon 12/9/19
28	✓	Trench for columns	5 days	100%	Mon 1/6/20
29	✓	Batton boards at gridlines	5 days	100%	Wed 1/8/20
30	✓	Layout trenching for walls	5 days	100%	Fri 1/10/20
31	✓	Trench building walls Footings	5 days	100%	Fri 1/10/20
32	✓	Set steel cages for columns anchor bolts and templates	5 days	100%	Fri 1/17/20
33	✓	Set steel and forms for footings	5 days	100%	Fri 1/17/20
34	✓	Place concrete for footings and columns	2 days	100%	Fri 1/31/20
35	✓	Area C Gridlines B-H 4-14	28 days	100%	Mon 1/6/20
36	✓	Stake building Corners and columns	2 days	100%	Mon 1/6/20
37	✓	Trench for columns	5 days	100%	Mon 1/13/20

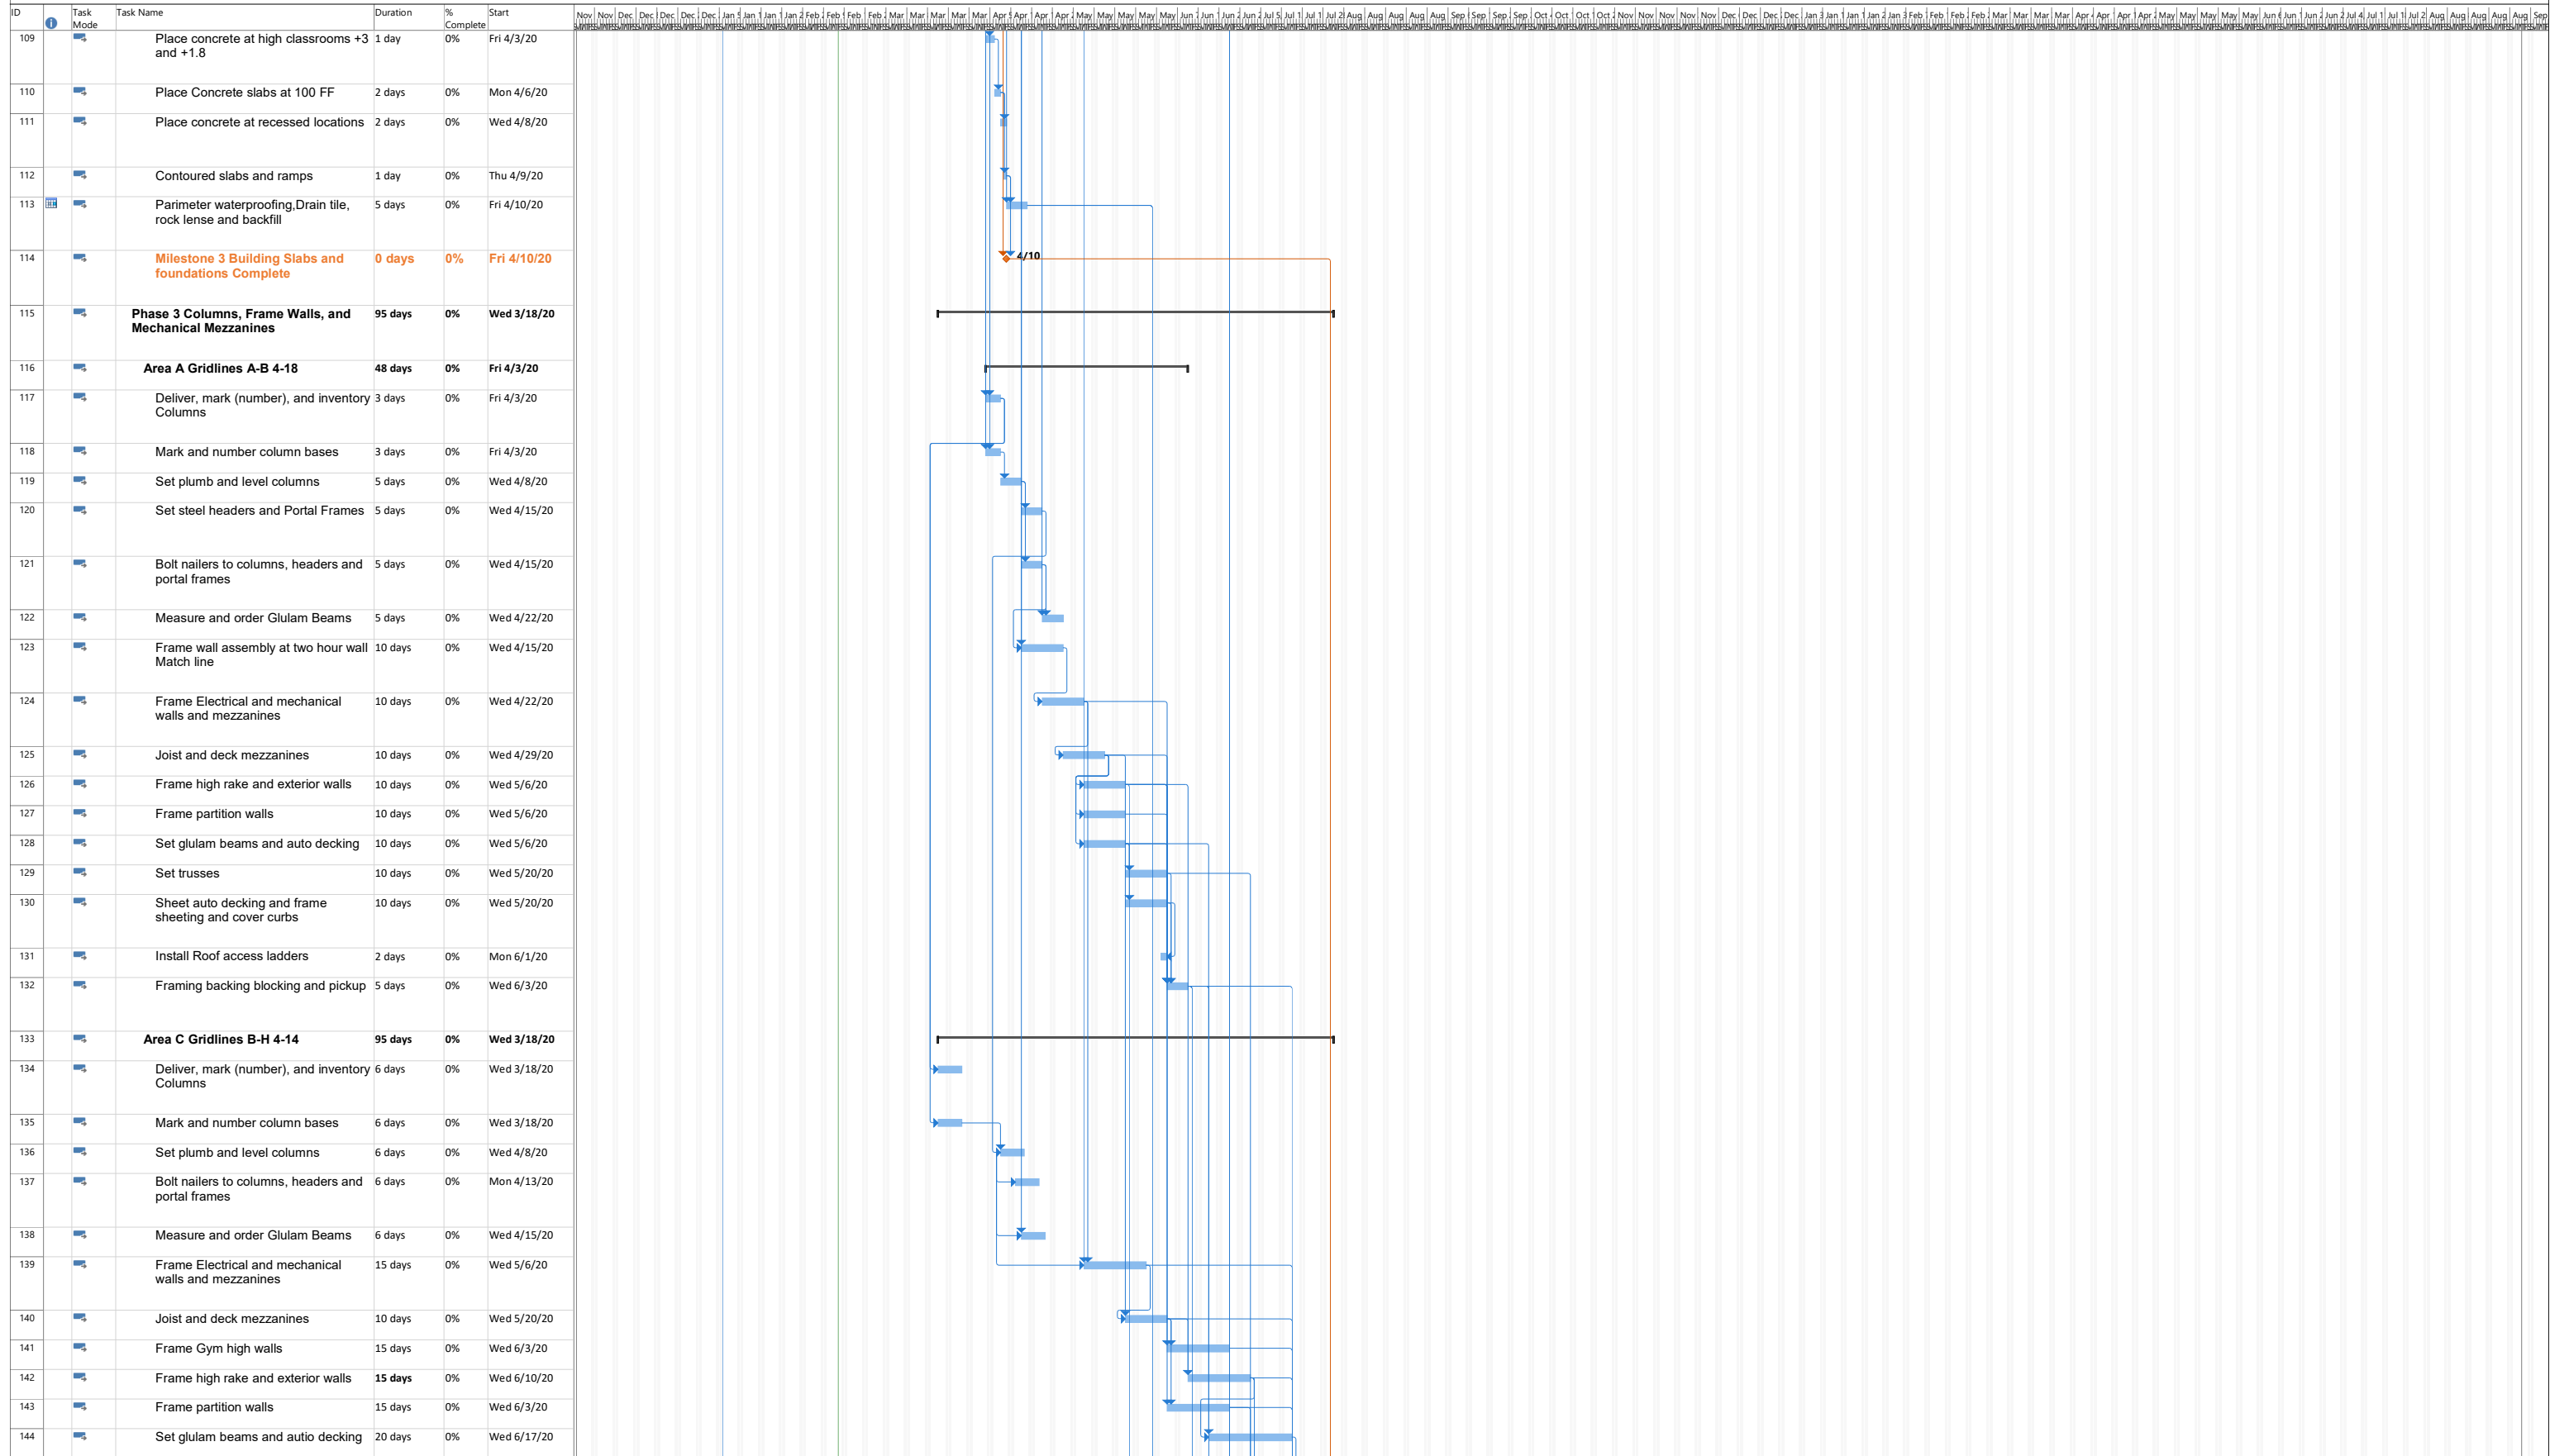

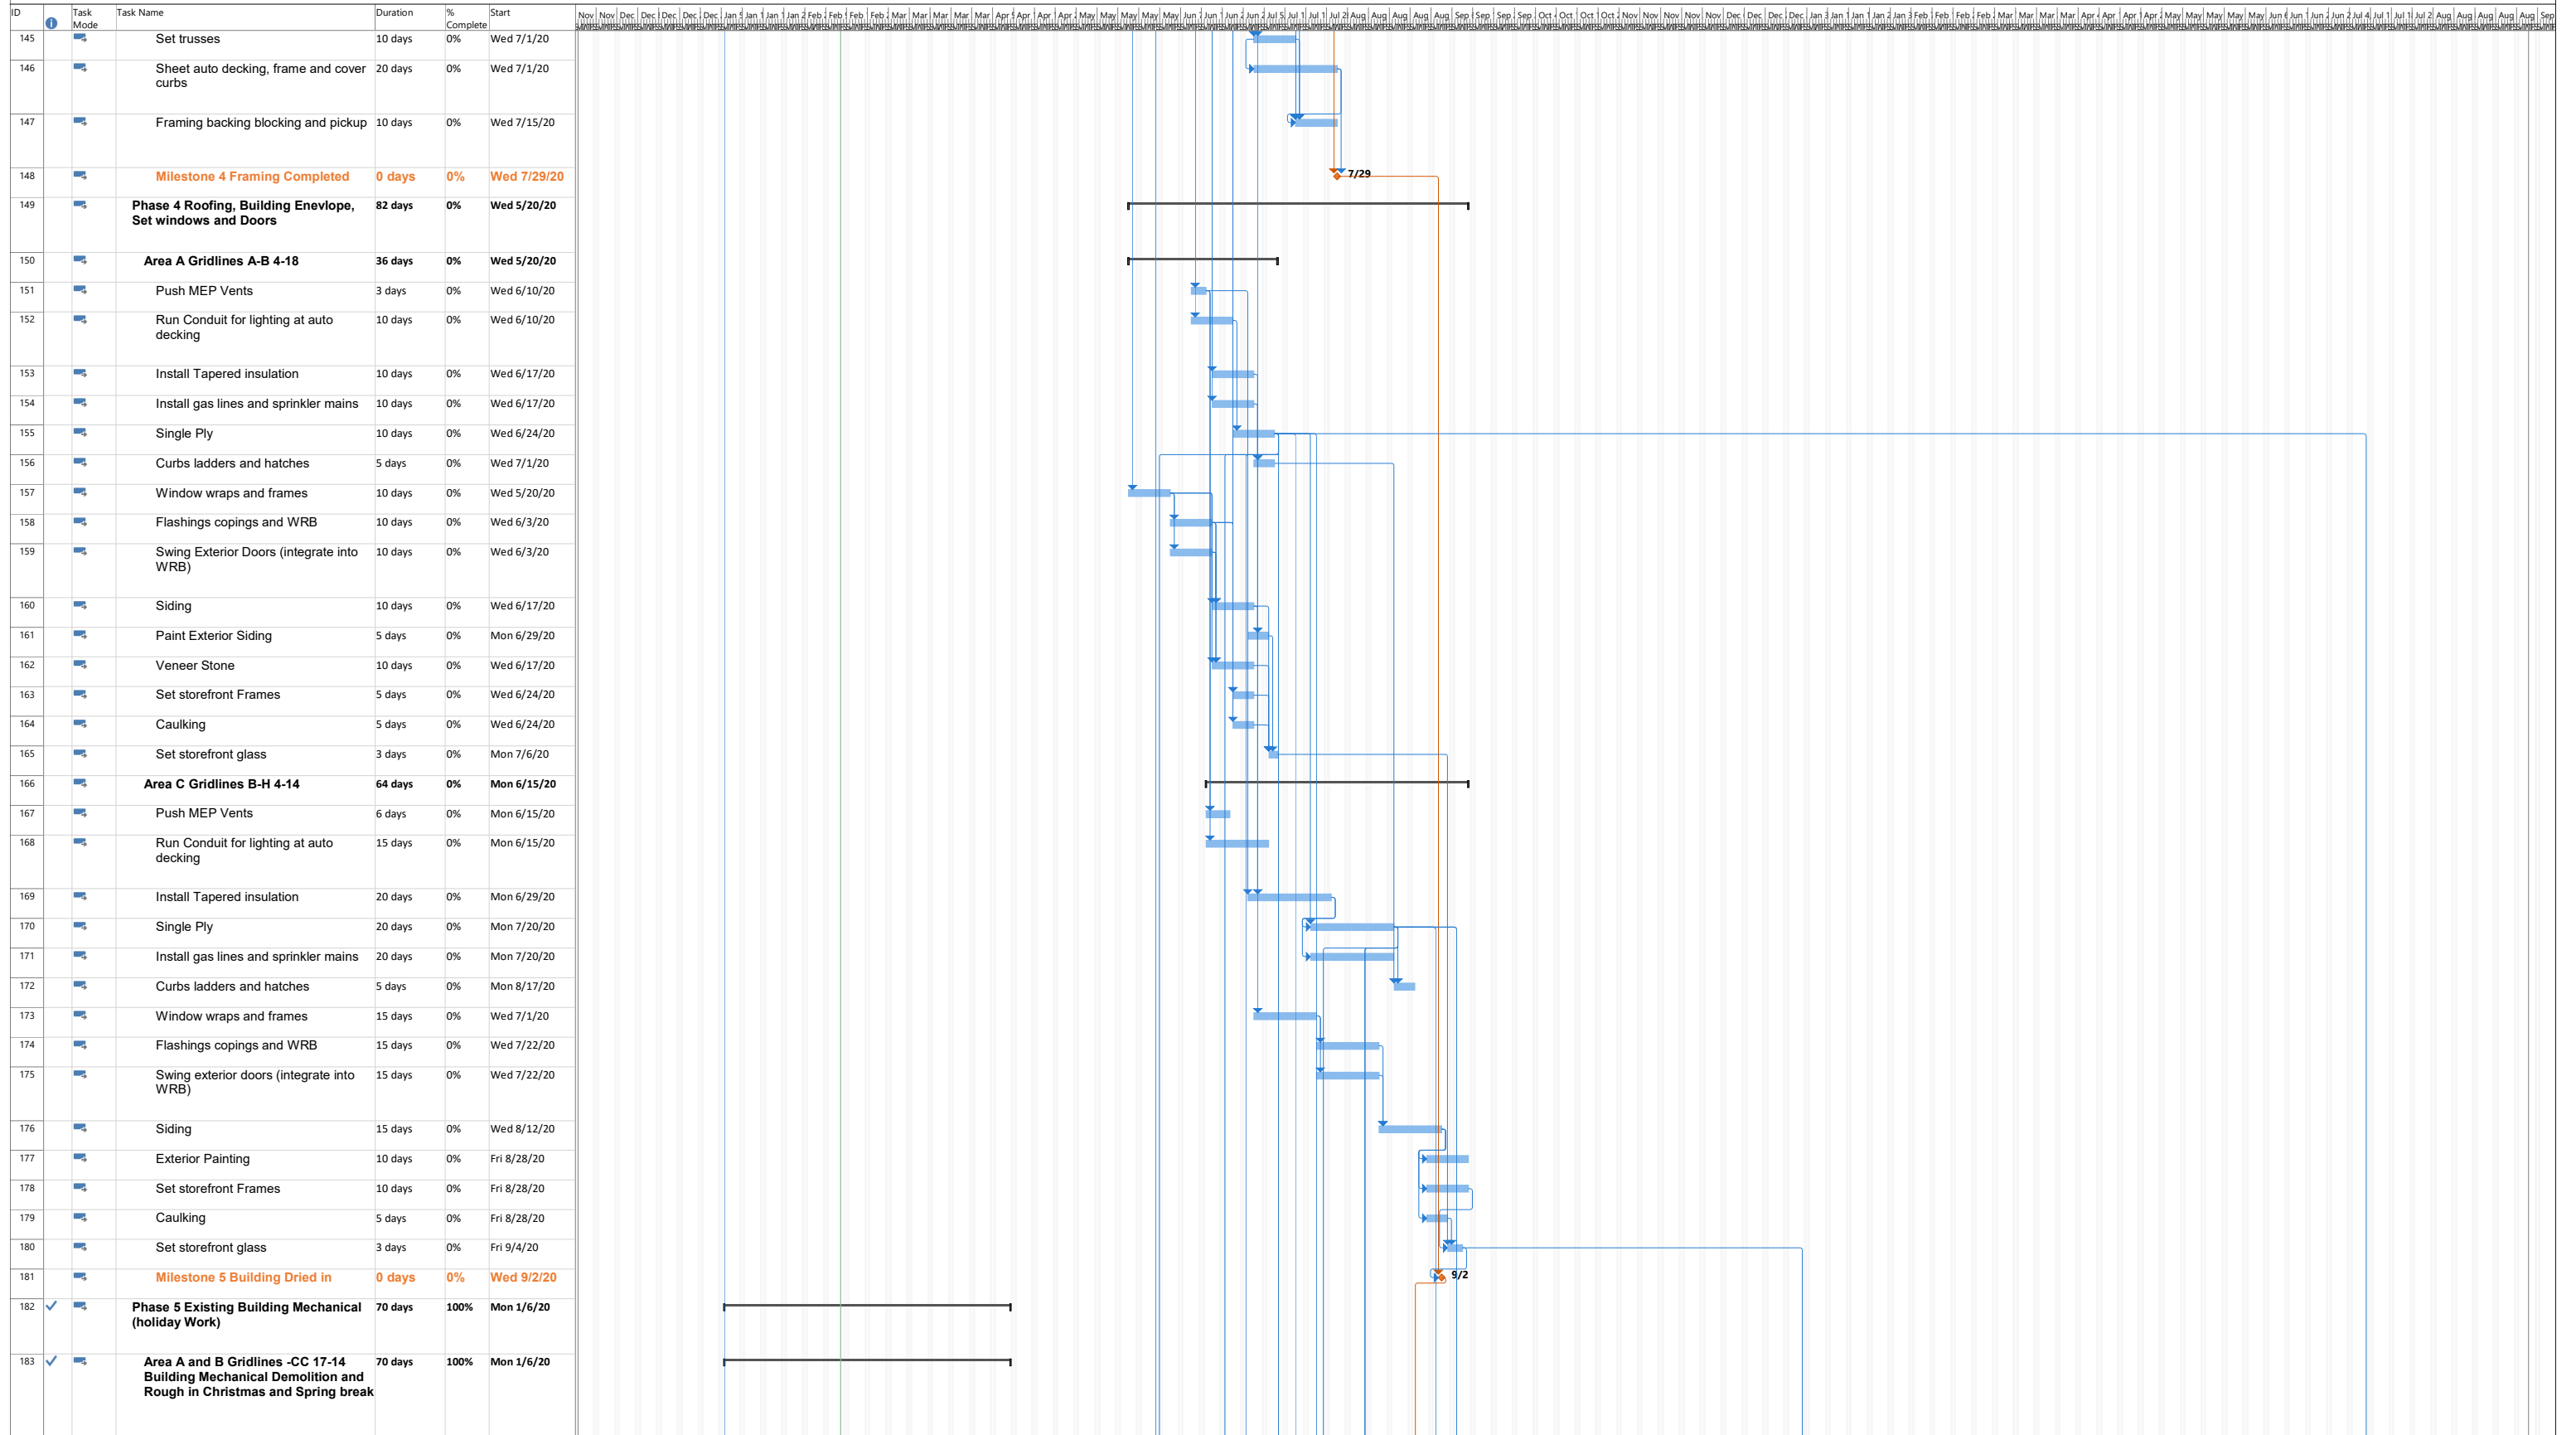

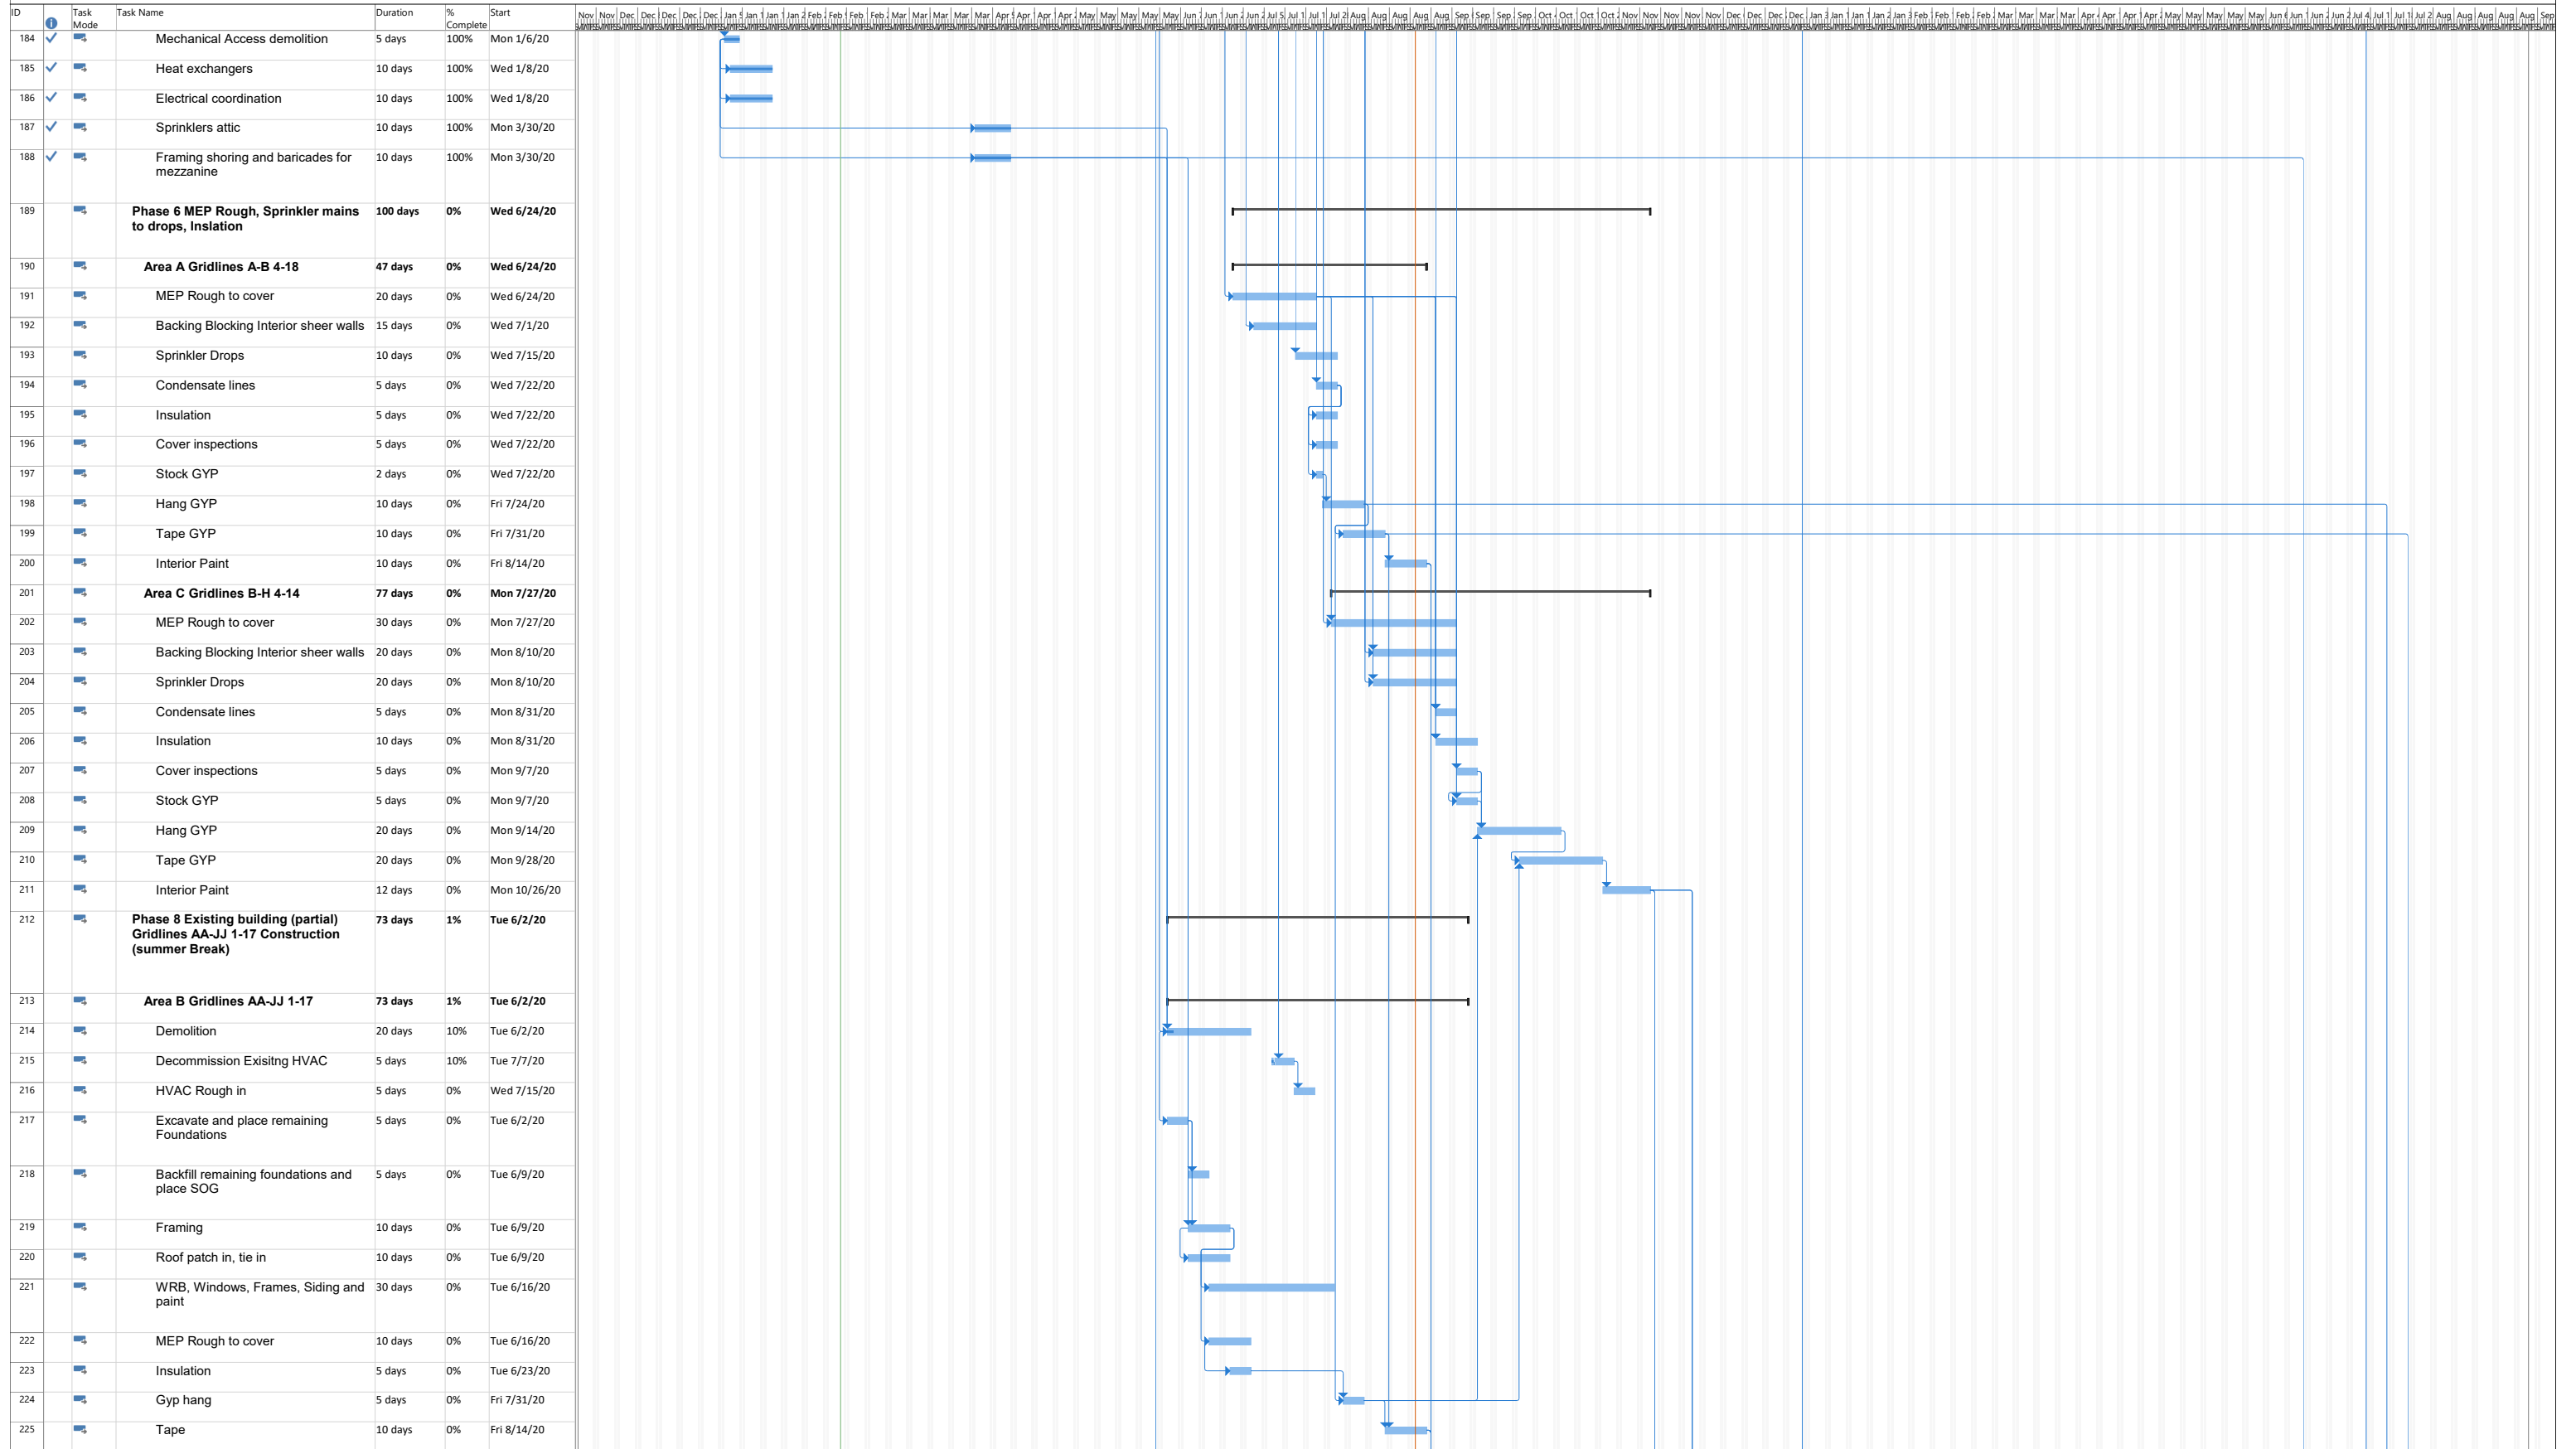

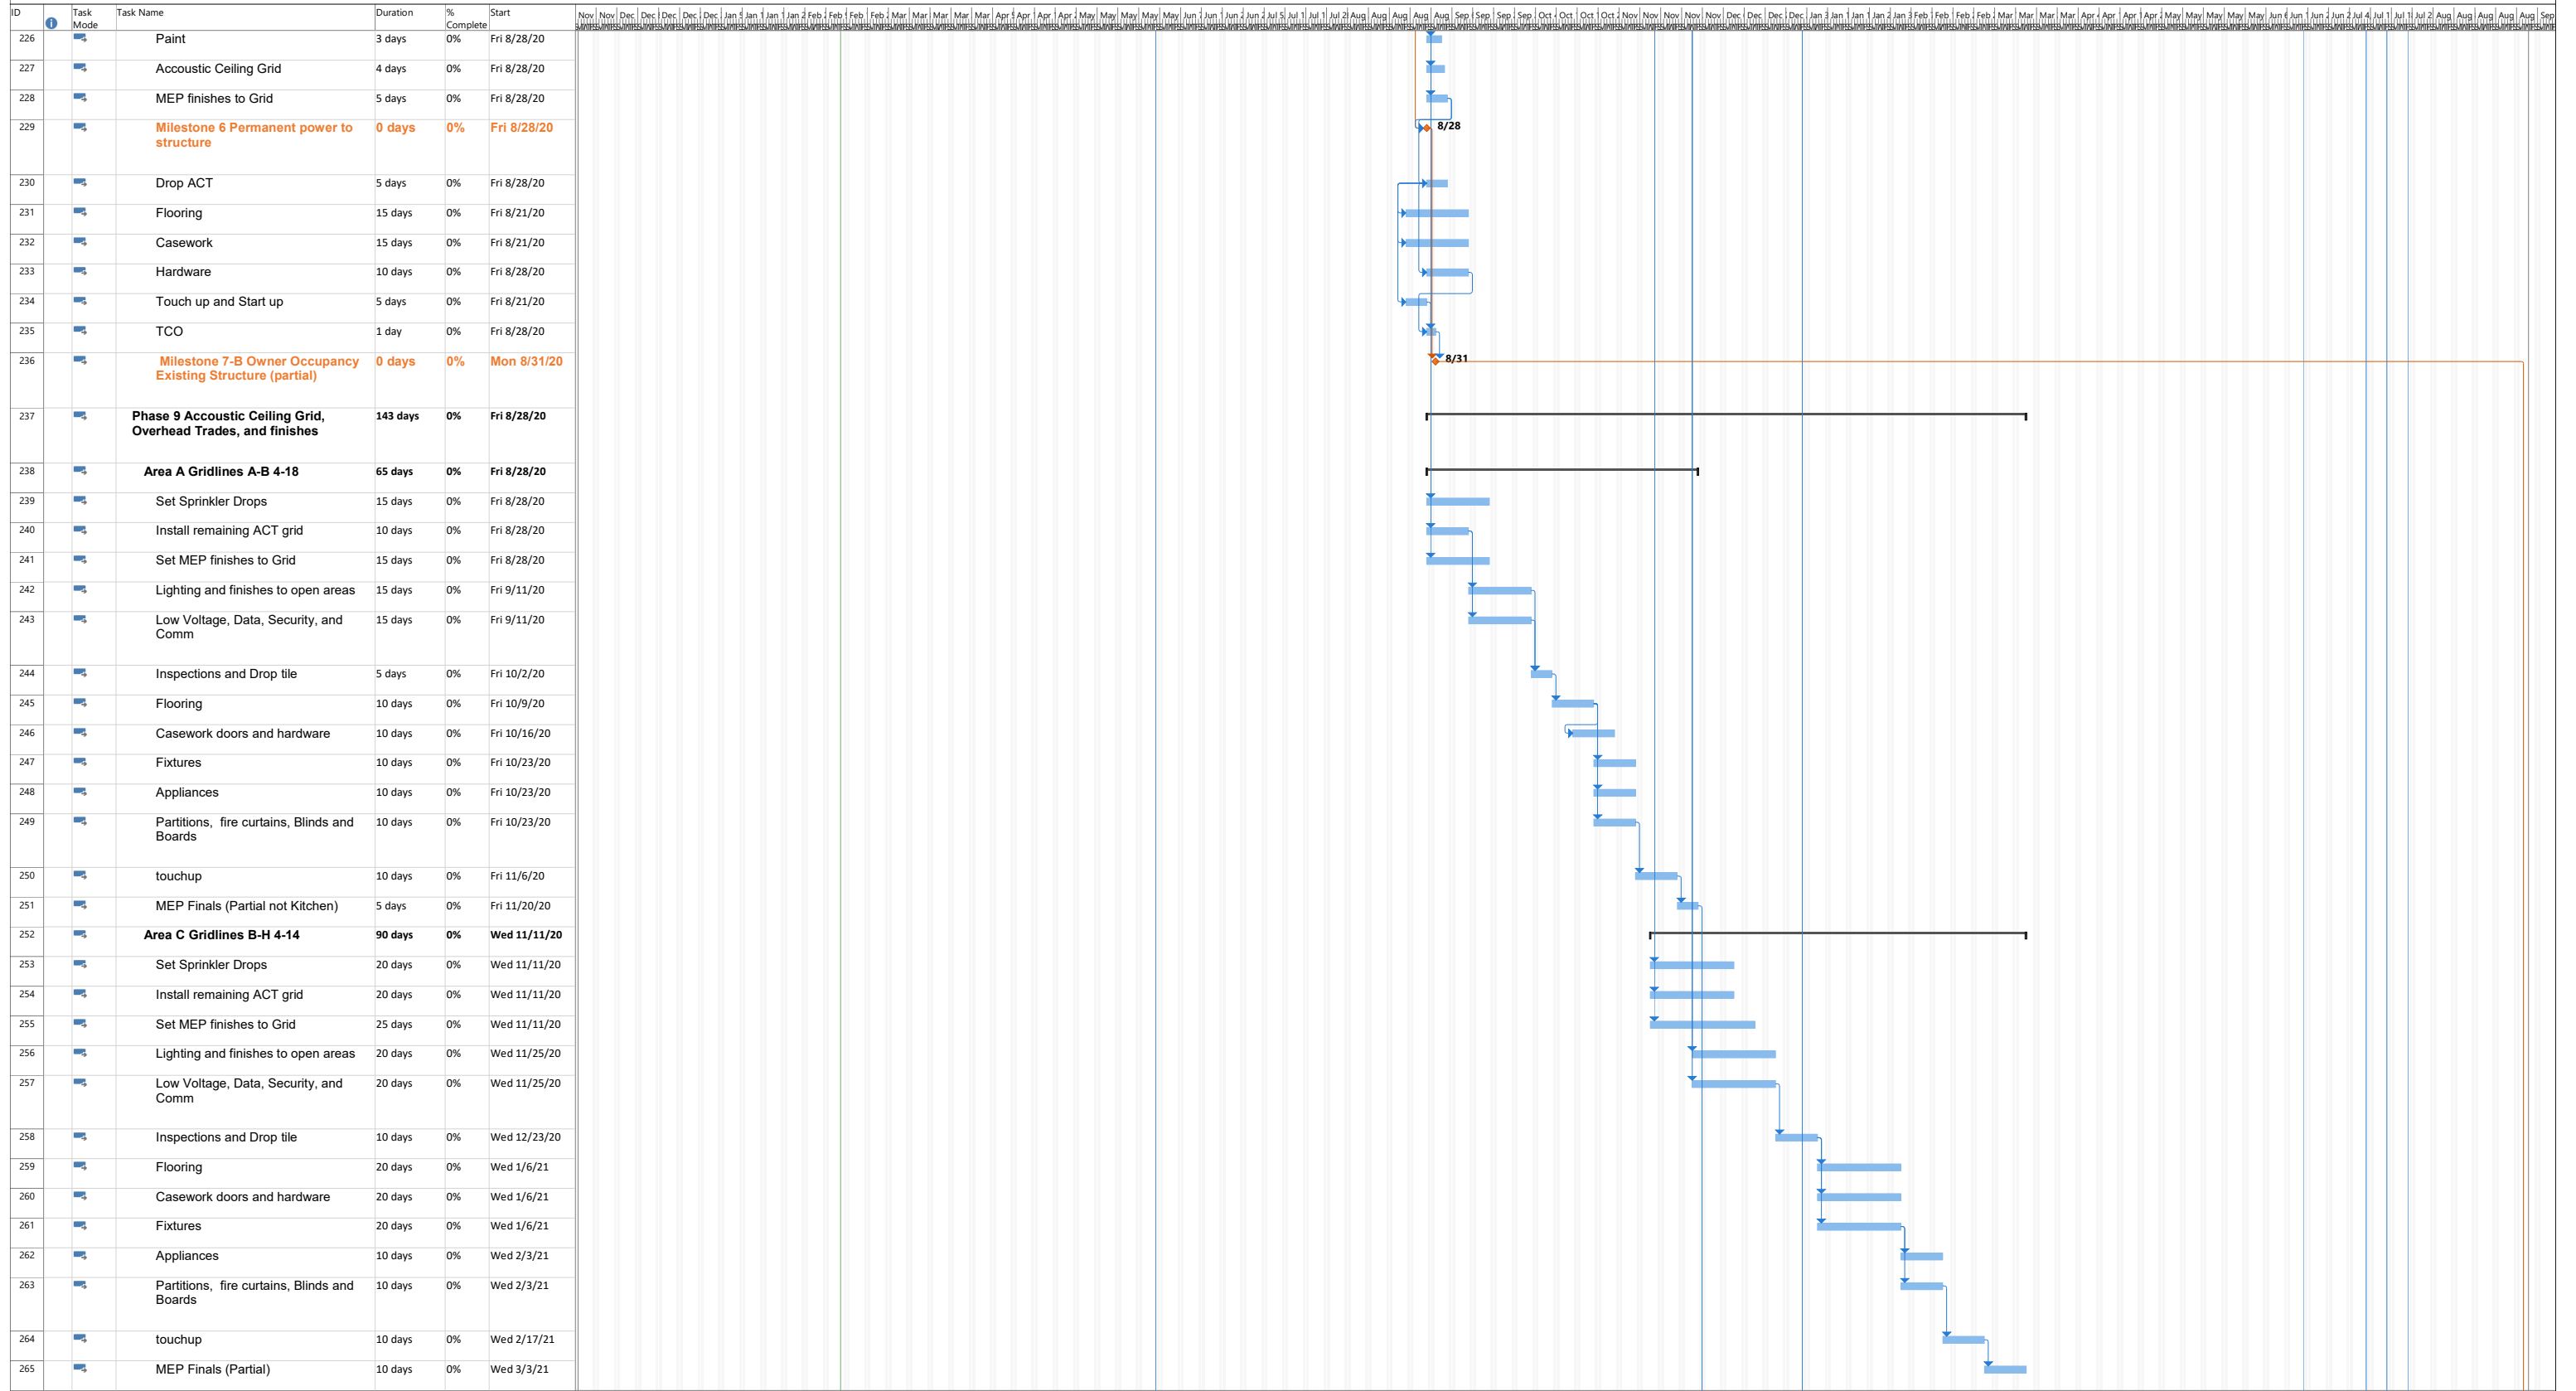

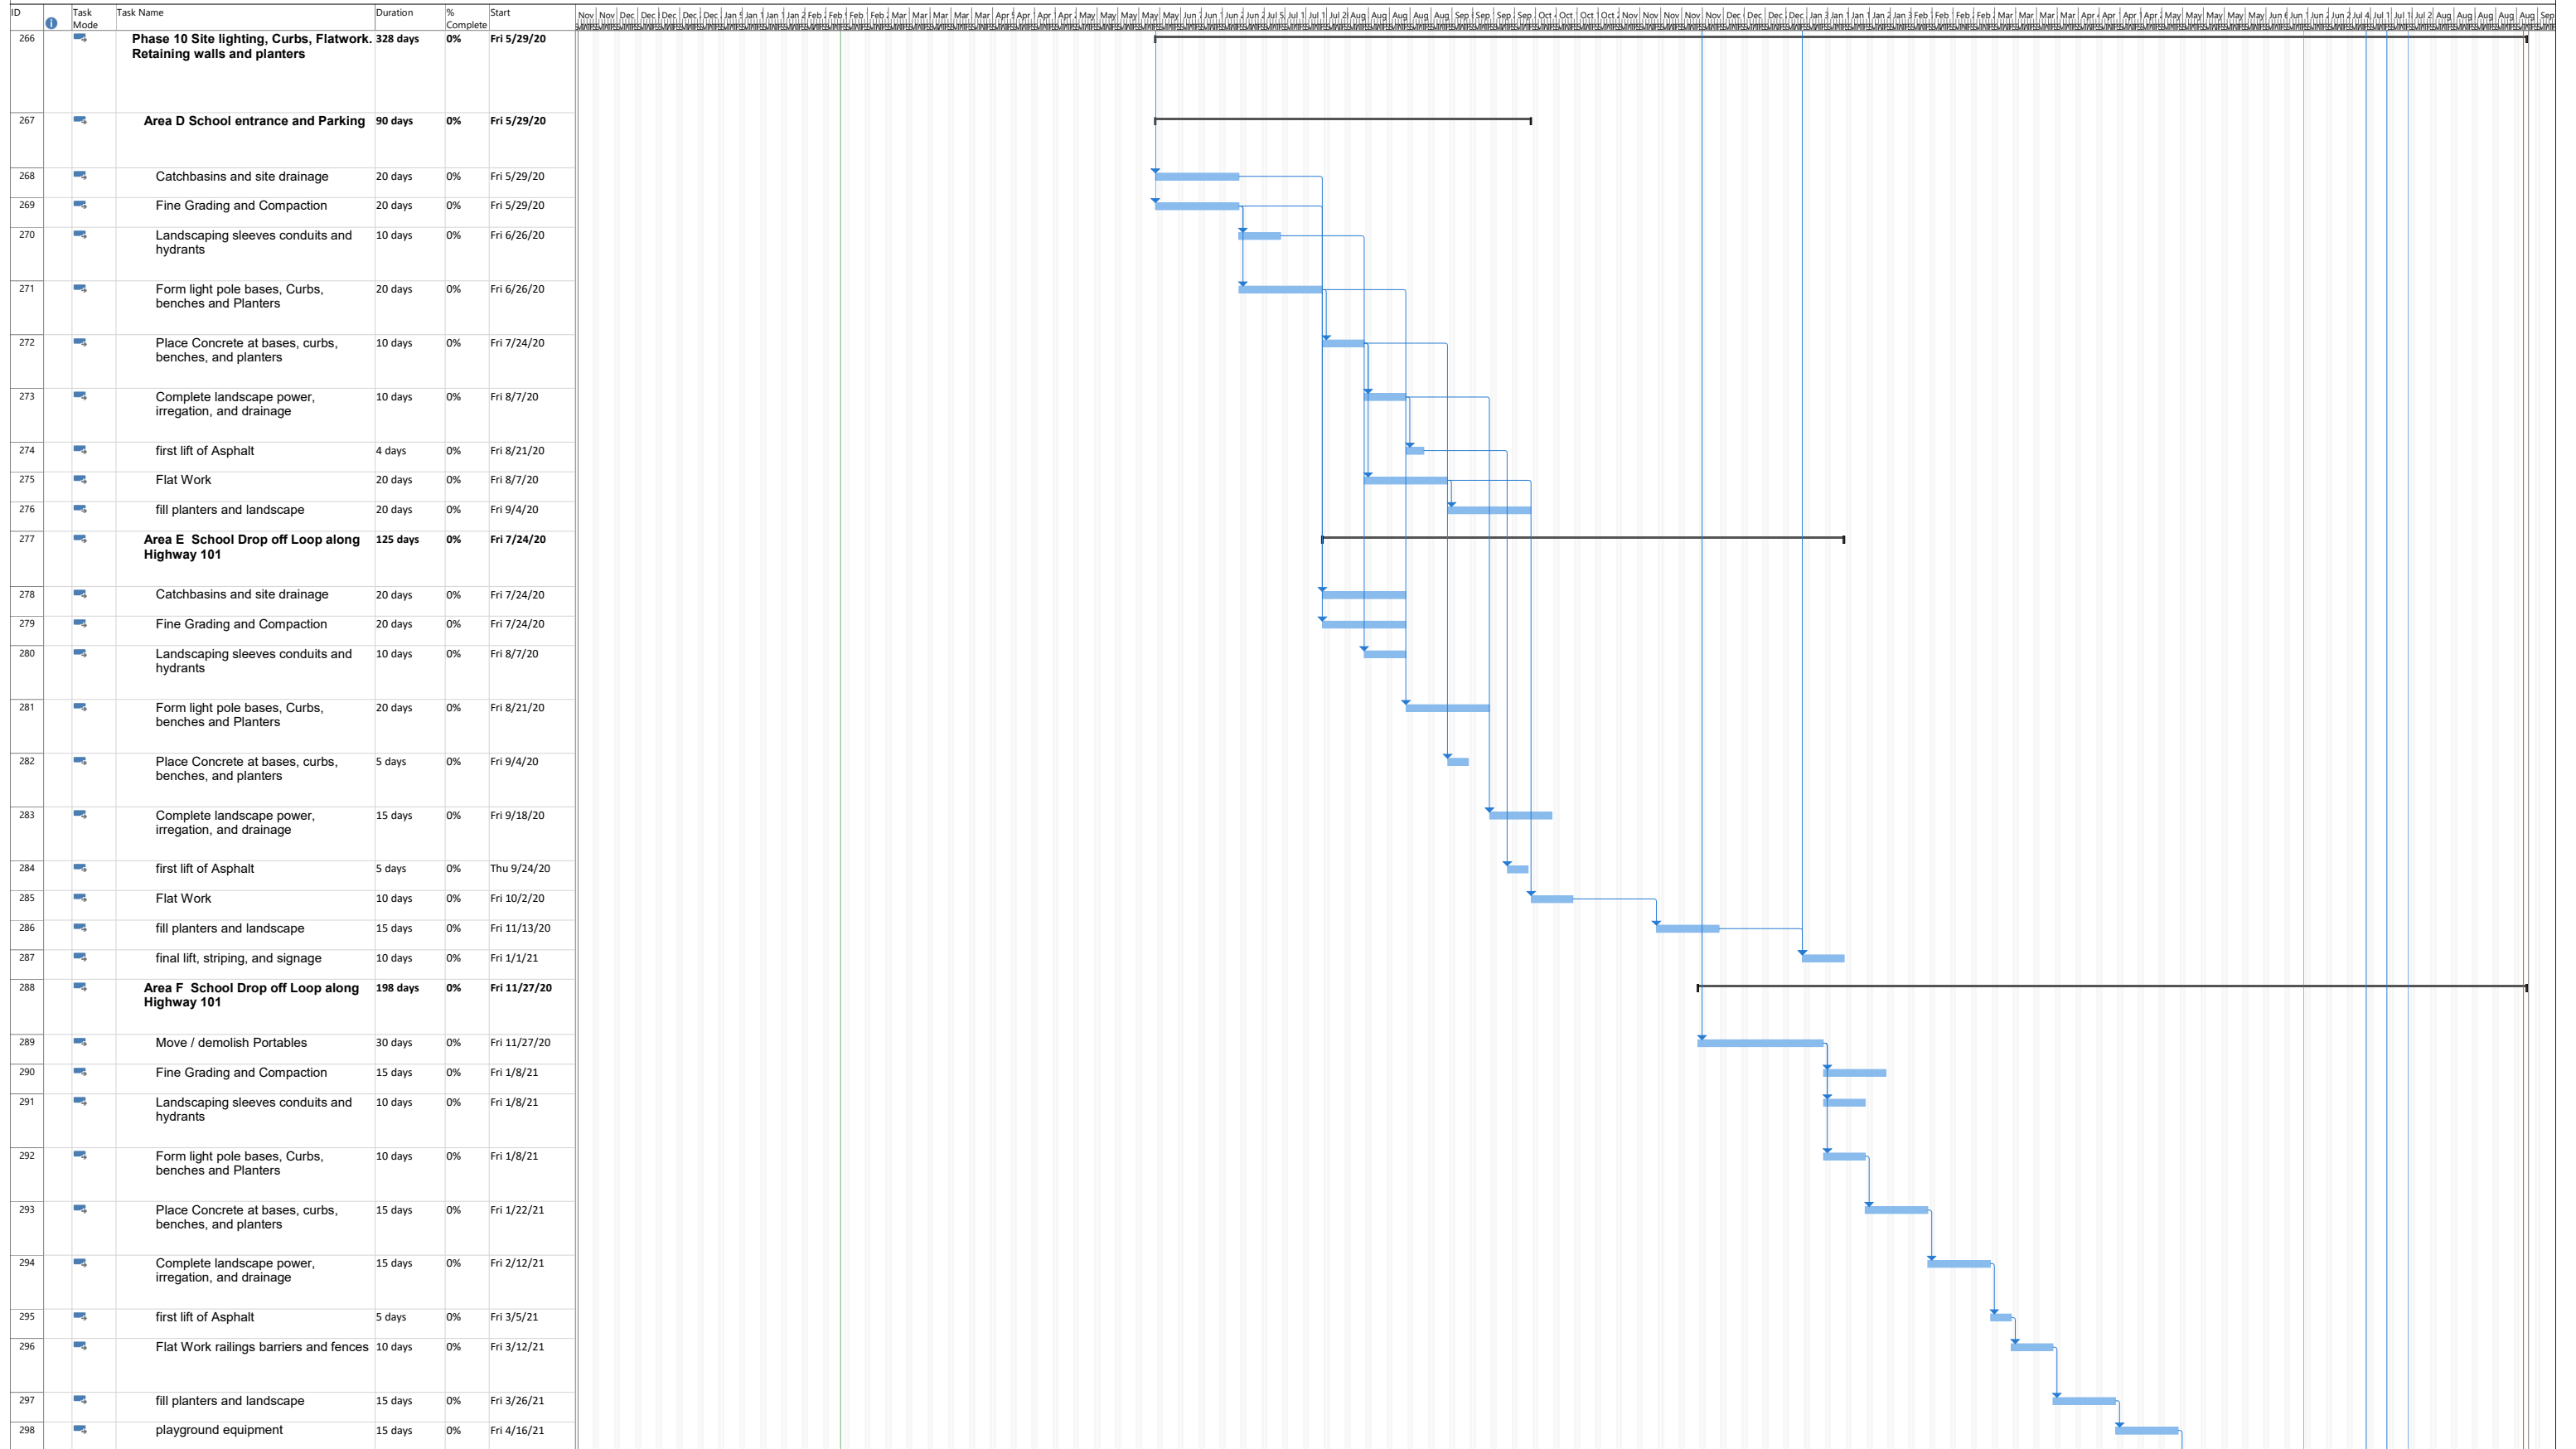

ID	Task Mode	Task Name	Duration	% Complete	Start
299		final lift, striping, and signage	5 days	0%	Fri 5/7/21
300		Finals	10 days	0%	Fri 5/14/21
301		Milestone 7AC Owner Occupancy New Structure	0 days	0%	Wed 9/1/21
302		Milestone 8 Substantial Completion	0 days	0%	Wed 9/1/21
303		Punch list	15 days	0%	Fri 5/14/21
304		Occupancy	5 days	0%	Fri 6/4/21
305		Final Completion entered into Warranty	0 days	0%	Wed 9/1/21
306		Phase 8 Existing building Gridlines AA-JJ 1-17 Construction (summer Break)	58 days	0%	Fri 6/11/21
307		Area B Gridlines AA-JJ 1-17	58 days	0%	Fri 6/11/21
308		Demolition	20 days	0%	Fri 6/11/21
309		Decommission Existing HVAC	5 days	0%	Fri 7/9/21
310		HVAC Rough in	5 days	0%	Fri 7/16/21
311		Excavate and place remaining Foundations	5 days	0%	Fri 6/11/21
312		Backfill remaining foundations and place SOG	5 days	0%	Fri 6/18/21
313		Framing	10 days	0%	Fri 6/18/21
314		Roof patch in, tie in	10 days	0%	Fri 6/18/21
315		WRB, Windows, Frames, Siding and paint	30 days	0%	Fri 7/2/21
316		MEP Rough to cover	10 days	0%	Fri 7/2/21
317		Insulation	5 days	0%	Fri 7/9/21
318		Gyp hang	10 days	0%	Fri 7/16/21
319		Tape	10 days	0%	Fri 7/23/21
320		Paint	2 days	0%	Fri 8/6/21
321		Accoustic Ceiling Grid	5 days	0%	Fri 8/6/21
322		MEP finishes to Grid	5 days	0%	Fri 8/6/21
323		Drop ACT	5 days	0%	Fri 8/6/21
324		Flooring	5 days	0%	Fri 7/30/21
325		Casework	6 days	0%	Fri 7/30/21
326		Hardware	6 days	0%	Fri 8/6/21
327		Touch up and Start up	10 days	0%	Fri 8/6/21
328		Final walk on existing structure	10 days	0%	Wed 8/18/21
329		Final Occupancy	10 days	0%	Mon 8/16/21
330		Milestone 7-B Owner Occupancy Existing Structure	0 days	0%	Wed 9/1/21

